Bruhat Bangalore Mahanagara Palike (BBMP)

Name of Work :- *Asphalting of Roads & Improvements to Footpaths at Someshwara Nagara, Sharada Nagara, MIG 3rd Phase and LIG sanitory core Yelahanka A sector, B Sector and Judicial Layout in Ward No.04 of Yelahanka new town sub division (Package No. 13)*

Sl No	Description of Work	Unit	BOQ Qty	Executed Qty
1	Removal & refixing stone slabs of drains and pointing in CM (1:3)	Sqm	1683.54	702.25
2	KSRRB 300-1 Earthwork excavation by manual means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications	cum	2616.49	3269.63
3	KSRRB M2100-10. Providing and laying Plain cement concrete of mix 1:3:6 with OPC @ 220kgs, with crushed 40mm and down size graded granite metal coarse aggregates @ 0.89cum and fine aggregates @ 0.46cum, in foundation mechanically mixed, placed in foundation and compacted by vibration including curing for 14 days including cost of all materials, labour. HOM curing, form works, scaffolding and centering complete as per specifications.	cum	1088.36	1080.49
4	KSRRB - M2300-14 Providing TMT steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining memebrs wherever necessary complete as per design (laps, hooks and wastage shall not be measured and paid) cost of materials, labour. HOM of machinery complete as per specifications.	Tonne	70.07	83.32
5	Providing and laying plain/reinforced cement concrete for side drains using M20 nominal mix concrete with OPC at 300 kgs. With 20mm and sown size granite metal course aggregates at 0.69 cum and fine aggregates at 0.43 cum machine mixed, well compcted for walls and bottom including centring shuttering cost of material HOM of machinary curing etc., complete excluding cost of steel as per MORTH specification.	cum	1138.93	1189.82
6	Providing and Fixing pre cast covering Slab 100mm thick made out of CC 1:2:4 and jelly 20mm Down size with steel reinforcement including form work,curing,including cost of alll materials, labour,hire charges of machinery, loading, unloading, lead and lift,transportation etc ,complete As per Engineer incharge.	Sqm	1716.24	2116.91
7	KSRB 5-8.2 Providing two line dressing to granite stone slab/granite stone masonry as per specifications. KBS 5.1.13	Sqm	1227.06	871.26
8	Providing and fixing RCC precast cover slab of 250mm thick for drain in cement concrete 1:1.5:3 using graded granite jelly 20mm and down size with steel reinforcement, including form work, lift charges, curing and concrete finished surfaces on both sides etc, complete and as per drawing and the directions of Engineer in-charge.	Sqm	134.40	93.60
	Providing and fixing pre cast solid cement concrete kerb stones made out of CC			

Vol-4

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ.
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-106

Sl No	Description of Work	Unit	BOQ Qty	Executed Qty
9	1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length finished with CM 1:3 plastering and finishing cutting including formwork, curing, including cost of materials, labour charges of machinery, loading and unloading, lead and lift, transportation etc.,complete.	Nos	6793.00	6731.00
10	Painting two coats after filling the surface with synthetic enamel paint in approved shades on new plastered concrete surfaces, with materials, labour complete as per specifications.	Sqm	940.80	1092.25
11	KSRRB M300-14. Excavation for roadwork in all types of soil by mechanical means including cutting and loading to tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and transportation with a lead of 1.00 km and complete as per specifications	cum	1873.26	1873.35
12	Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing coarse graded crushed stone aggregates of granite/ trap/basalt material, mixing in a mechanical mix plant at OMC, Carriage of mixed material to work site, spreading in uniform layers with motor grader on prepared surface and compacting with vibratory power roller to achieve the 98 % proctor density. complete as per specifications.	cum	936.63	936.67
13	KSRRB M400-17. Providing, laying, spreading and compacting cushed stone aggregates of granite / trap / basalt to wet mix macadam specifications including pre mixing the material with water at OMC in mechanical mix plant carriage of mixed materials by tipper to site, laying in uniform layers with paver in sub-base/base course on well prepared surface and compacting with vibratory roller to achieve the desired density complete as per specifications.	cum	1404.94	1405.01
14	KSRRB M500-6. Providing and applying primer coat with S.S. bitumen emulsion on prepared surface of granular base such as WMM including cleaning of road surface and spraying primer at the rate of 0.60 kg / sqm using mechanical means complete as per specifications.	Sqm	6244.20	6244.49
15	KSRRB 500-2. Cleaning the existing black topped surface with brooms, soft brushes and finally dusting with old gunny bags and / or compressed air to receive bituminous treatment including cost of all materials, labour, HOM complete as per specifications.	Sqm	8372.30	10465.26
16	KSRRB M500-17. Providing and laying dense graded bituminous macadam using crushed aggregates of specified grading, premixed with VG30 grade bituminous binder and, transporting the hot mix to work site, laying to the required grade, level and alignment, rolling with smooth wheeled, vibratory and tandem rollers to achieve the desired compaction in all respects complete as per specifications Clause 505 of MORTH V revisionusing 40/60 TPH capacity H.M.P. with Mechanical paver Gr-II (50 mm to 75 mm) with 4.5 % VG-30 Bitumen	cum	312.21	312.22
	KSRRB 500-7. Providing and applying tack coat using 80/100 grade bitumen(VG10) on the prepared black topped surfaces at 2.5 kg per 10 sqm,			

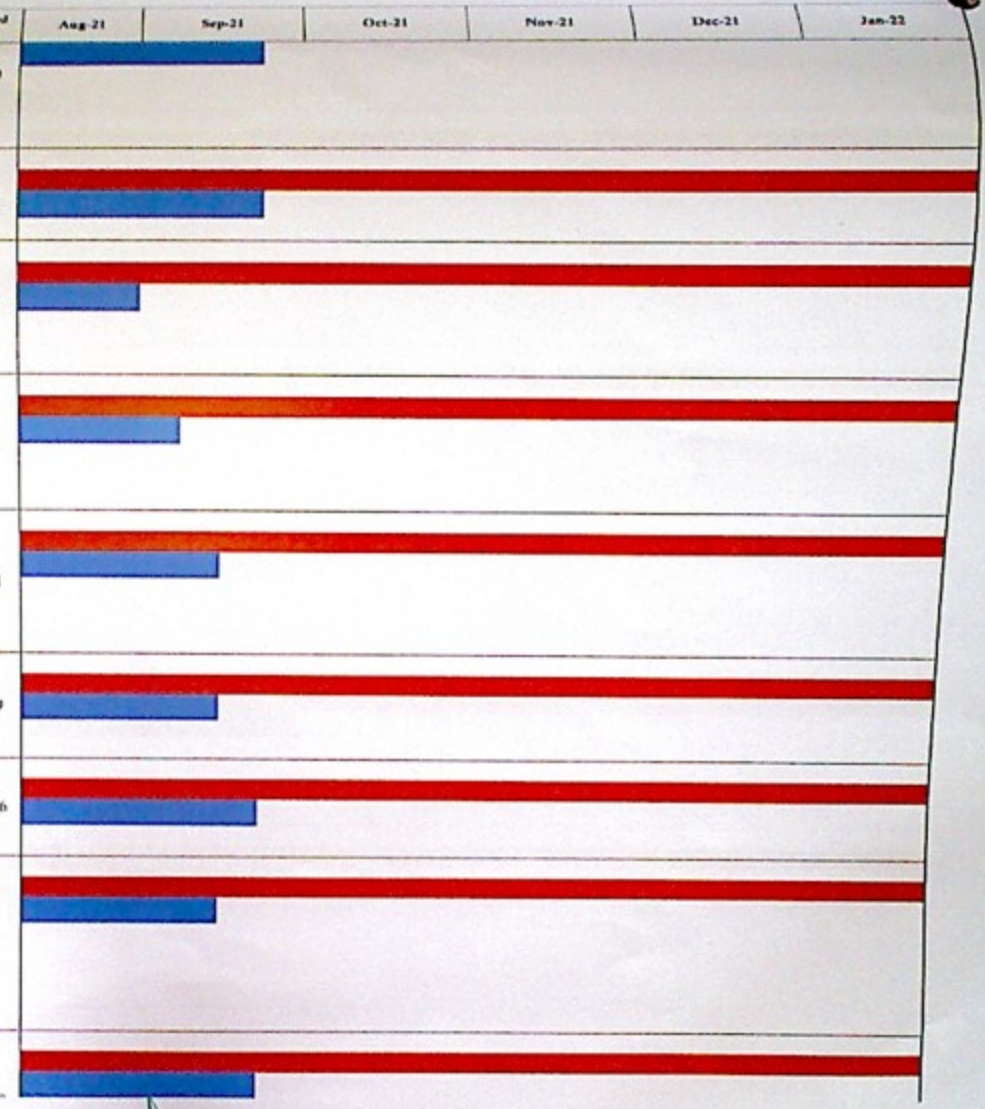

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-106

Sl No	Description of Work	Unit	BOQ Qty	Executed Qty
17	heating bitumen in boiler fitted with spray set (excluding cleaning of road surface) including cost of all materials, labour, HOM complete as per specifications.	Sqm	20081.89	17147.20
18	Providing and laying bituminous concrete 40mm thick with hot mix plant, using crushed aggregates of specified grading, premixed with bituminous binder and filler, transporting the hot mix to work site, laying with a paver finisher to the required grade, level and alignment, rolling with smooth wheeled, vibratory and tandem rollers to achieve the desired compaction in all respects complete as per specifications. Clause 507 of MORTH V revision as per IRC SP-53-2015 using 40-60 TPH capacity HMP with mechanical paver grading II (30-45mm) with 5.4 % of modified bituminus binder consisting of 4.97% of VG-30 bitumen (60/70 grade) and 0.43% of plastomeric thermoplastics (waste plastic)	cum	794.93	685.65
19	KSRRB M800-13 Road Marking with Hot Applied Thermoplastic Compound with Reflectrising Glass Beads on Bituminous Surface/ Concrete Surface Providing and laying of hot applied thermoplastic compound 2.5 mm thick including reflectorising glass beads at 250 gms per sqm area, thickness of 2.5 mm is exclusive of surface applied glass beads as per IRC:35 standards specified. The finished surface to be level, uniform and free from streaks and holes complete as per specifications.	Sqm	699.20	630.40
20	KSRB 4-1.6 Providing and laying in position plain cement concrete of Mix 1:2:4 with OPC @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.878 cum and fine aggregates @ 0.53cum, machine mixed, concrete laid in layers not exceeding 15 cms thick, well compacted, in foundation, plinth and cills, including cost of all materials, labour, HOM curing complete as per specifications.	cum	86.36	18.34
21	KSRB 5-14 Providing and constructing load bearing wall with solid concrete blocks of size 400x200x200 mm having block density not lessthan 1860 kg/m3 and having a minimum average compressive strength 4.00 N/mm2 confirming to IS 2185 (Part1 2005 and constructed with CM 1:4 , as per IS 2572:2005 including cost of all materials, labour charegs, scaffolding, curing complete as per specifications.	Sqm	113.38	82.05
22	KSRB 14.6 Providing and laying heavy duty cobble stones interlock pavers, 60mm thick using cement and course sand for manufacture of blocks of approved size, shape and colour with a minimum compressive strength of 281 kg per sqm over 50mm thick sand bed (average thickness) and compacting with plate vibrator having 3 tons compaction force thereby forcing part of sand underneath to come up in between joints, final compaction of paver surface joints into its final level, including cost of materials, labour and HOM complete as per specifications.	Sqm	3697.68	3554.26

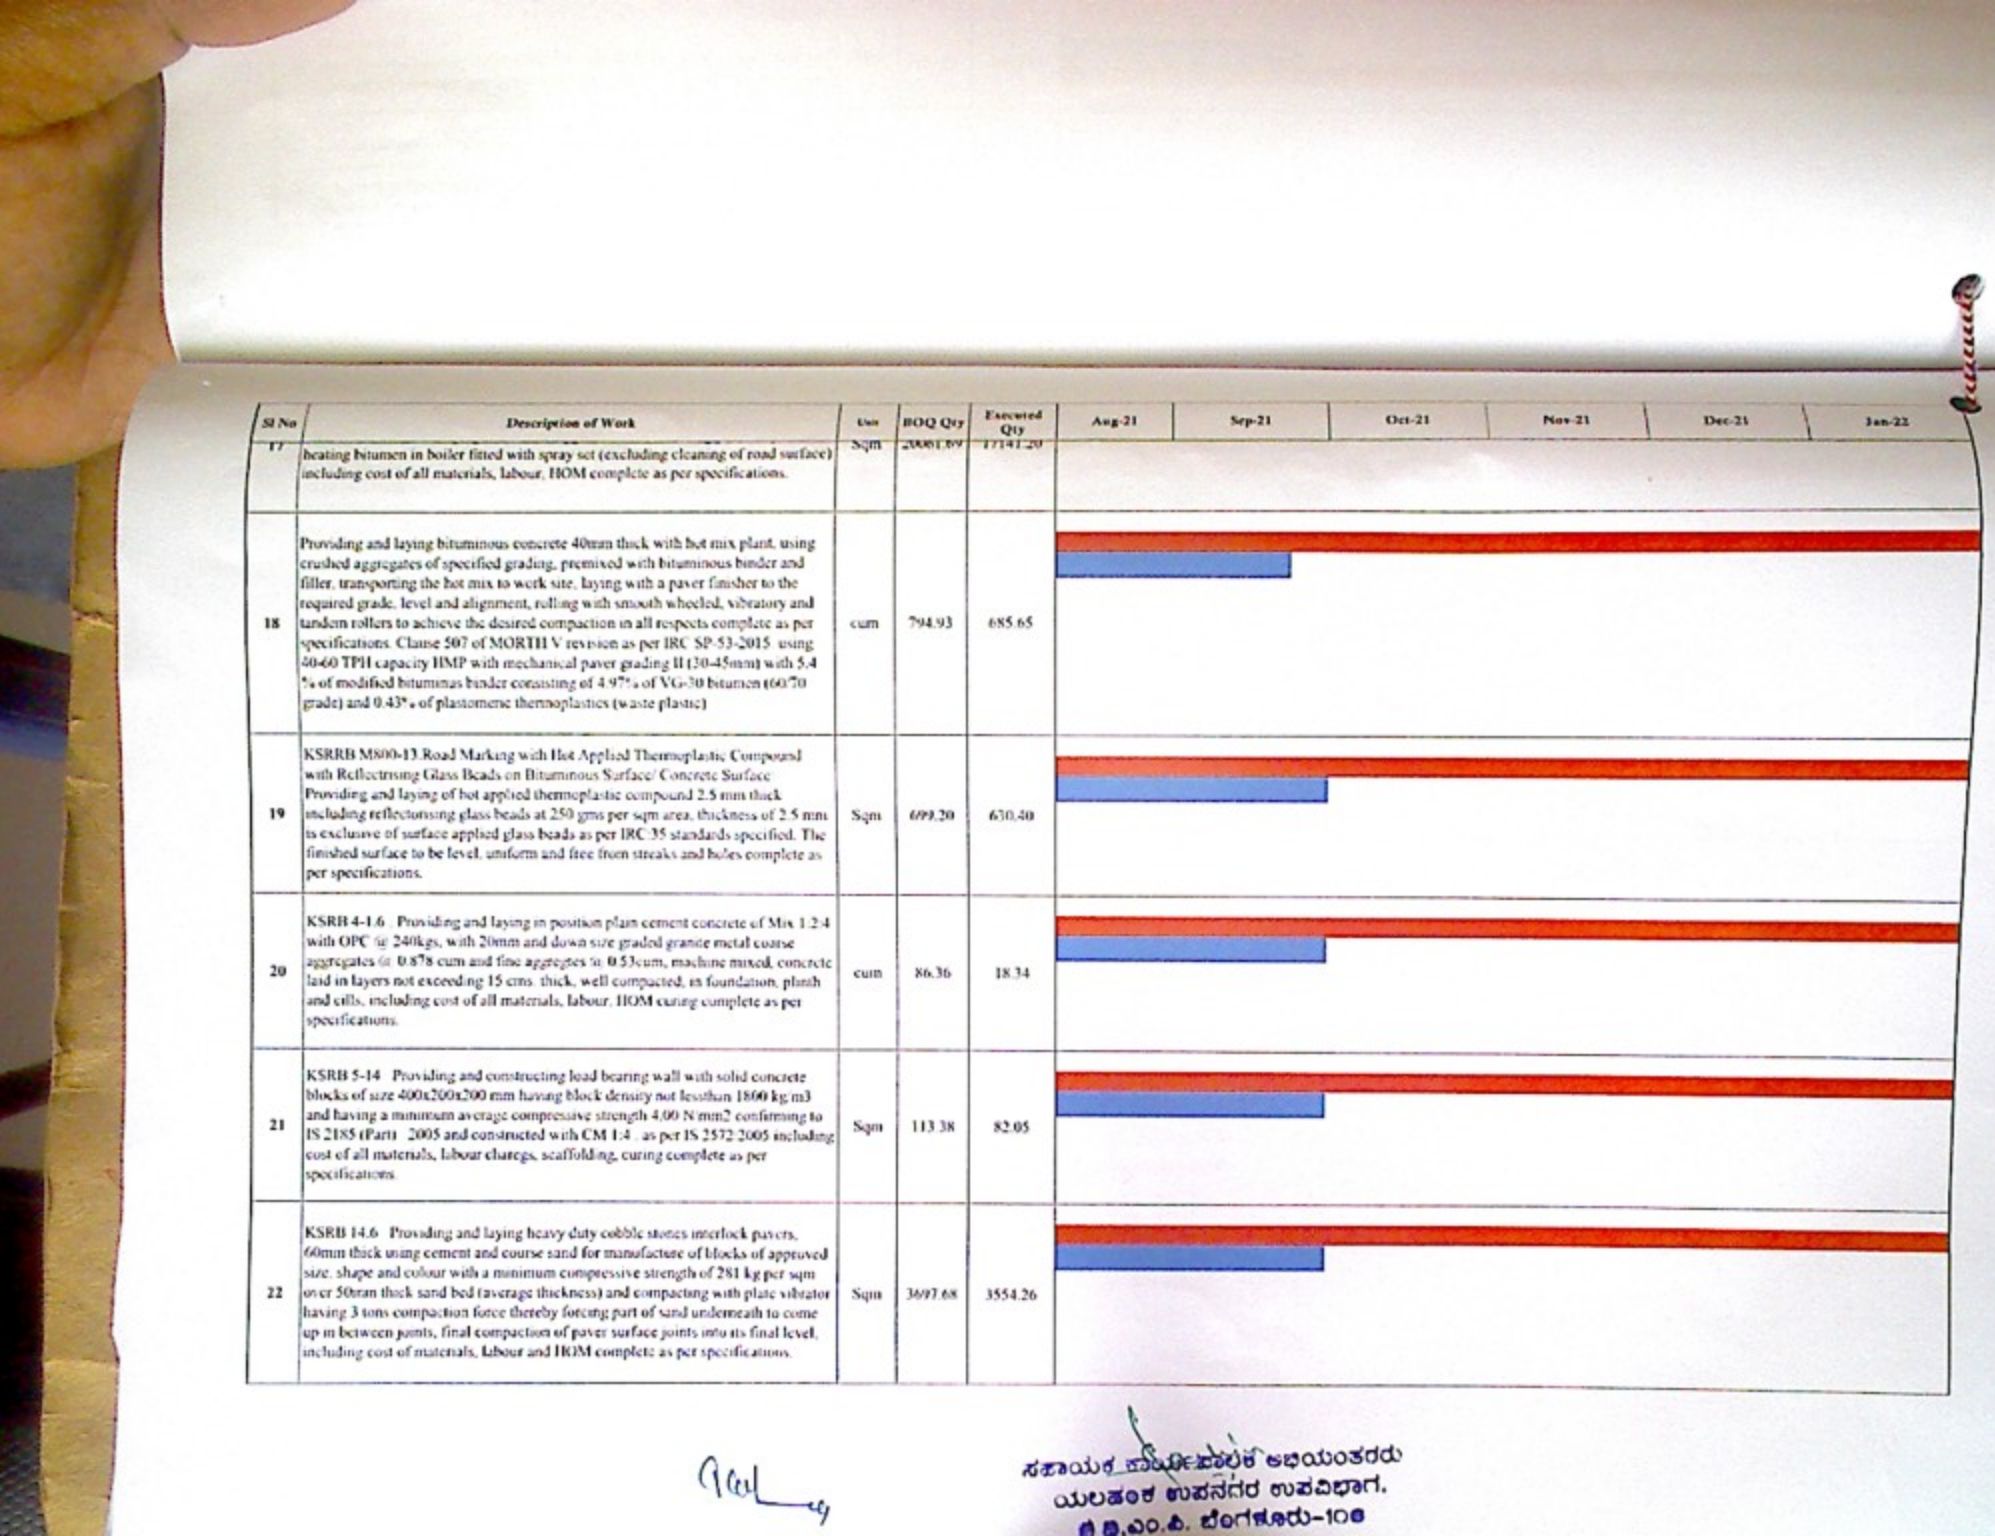

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ,
ಬಿ.ಬಿ.ಎಂ.ಪಿ, ಬೆಂಗಳೂರು-106

Sl No	Description of Work	Uni	BOQ Qty	Executed Qty
23	Supply and fixing of Retro Reflective Single Arrow Road NameSignboard of size 1600mm x 900mm made out of retro reflective sheeting conforming to Type XI standards of ASTM D 4956 - 09 & as per IRC 67-2012 for full back ground of blue colour & white letters and fixed over 4 mm thick Aluminium Composite Material sheet having minimum 0.5 mm thick Aluminium skin on both sides with back side painted grey colour and fixed over back support frame SS angle of 15mm x 20mm x 1.2mm, supported by 38mm OD stainless steel pipe all round in 304 grade and 2 nos of vertical posts of 50 mm OD stainless steel pipe of 202 grade firmly fixed to the ground by means of properly designed foundation of size 450mm x 450mm x 600mm in 1:1.5:3 ratio cement concrete. The background shall be blue in color with letters and border in white,the item includes earthwork excavation, cost of all materials, loading,unloading, lead, lift, transportation etc., complete as per direction of engineer incharge of work clause 6.9 of IRC 67-2012 for Type XI retro reflective sheeting from the sheeting manufacturer & a certified copy of test reports from an independent test laboratory conforming to clause 6.7 of IRC 67-2012 including outdoor weather exposure report for the retro reflective sheeting offered shall be submitted by the contractor for technical qualification in the tender	Sqm	8.64	8.64

Contractor representative

Assistant Engineer

Consultant representative

Assistant Executive Engineer
